


Tranche 3 (20%): Price date plus 9 months (2015)	(ii) Evidence of engagement with key stakeholders																			
	(iii) Baseline report																			
	(iv) Pre-analysis Plan indicating main outcome variables, empirical strategy and subgroup analyses, etc. (in 3ie format)																			
	(v) Qualitative study report																			
	(vi) Midline survey questionnaire																			
Tranche 4 (20%): Prior due date plus 12 months (April 2016)	(i) Progress report and PIP (in 3ie format), including fund utilization statements																			
	(ii) Evidence of engagements with key stakeholders																			
	Coding midline questionnaire into CAPI & pre-testing, recruitment & training enumerators, data collection																			
	(iii) Midline survey report including descriptive analyses and midline impact estimates																			
	(iv) End line survey questionnaire																			
Tranche 5 (20%): Prior due date plus 12 months (April 2017)	(i) Progress report and PIP report (in 3ie format), including fund utilization statements																			
	(ii) Evidence of engagement with key stakeholders																			
	(iii) End term survey progress report																			
	(iv) Draft final report in (3ie format) stating explicitly actionable policy recommendations emerging from the study																			

Colour	Activity
Green	Preparatory activities (design intervention & randomisation, PIP, other prep)
Orange	Sampling/site identification
Blue	Survey
Purple	Awareness Creation & Promotion Campaign
Red	Reporting/D&D

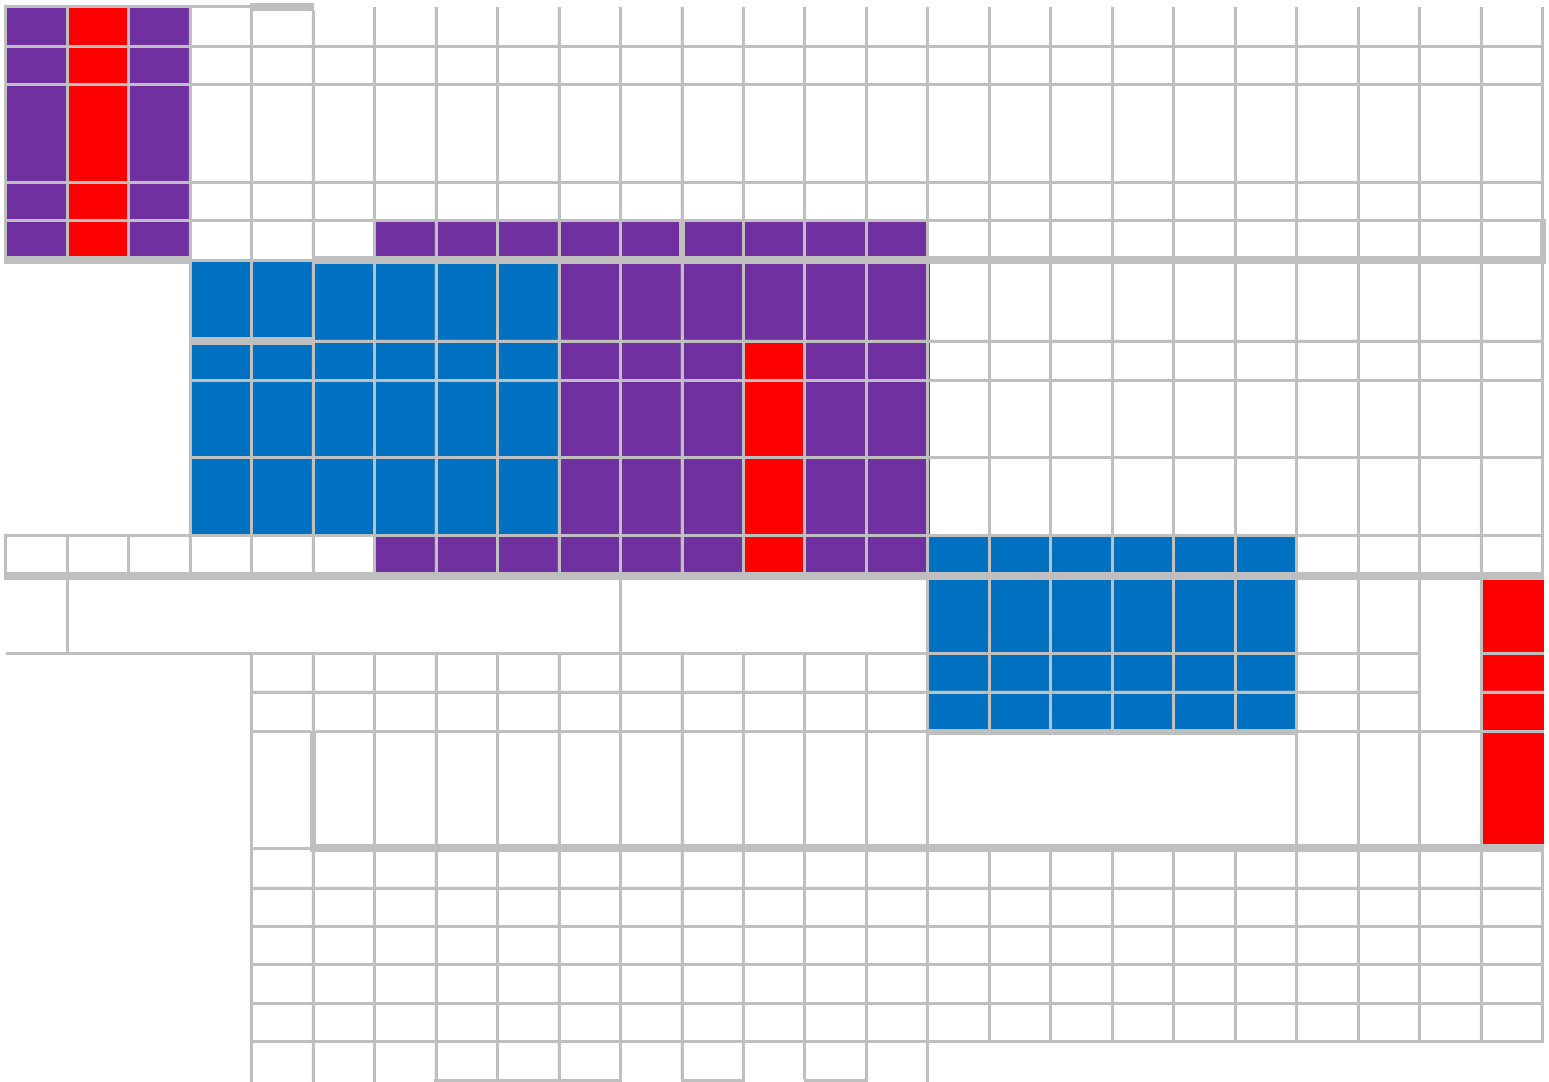

COMMENT ON PROGRESS

Agreements signed although this was late by one month

done as per plan

PIP submitted, but received feedback that format was not current one. So to revise and submit in the new format

Done: this report

Done: delivered as expected with this report

Done

Done: delivered as expected with this report

This has not been altered - as per original proposal - more explanation given on parameters in excel file

Done: qualitative questions included in household questionnaire; Check list for FGD prepared

Done: delivered as expected and with this report

Done: this report

Not required, one PI and IA are from Uganda and working in Institutions that are mandated to carry out evaluations.

Done: meetings to refine design of intervention and plan implementation of activities held with AGRA's M&E and AGRA's PASS programs, as well as the implementing agency (PSL);

Done: I have provided - notes/emails as proof of meetings with AGRA, PSL

Done: see financial report attached

Done: see the proposal on the intervention which has been prepared by the study team and IA, and with involvement of AGRA team

Done: this report

Done: this report

Done: this report

Partly done in revised proposal. Unfinished because PhD student will join Wageningen in second year of project. Her proposed analysis will form part of pre-analysis plan which is due by December 2015

Done part of the baseline report

Done: delivered as expected with this report

Planned Activities for Next Reporting Period (June 2015 to April 2016)

Planned Activities for Reporting Period (May 2016 to April 2017)
